


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Cost	Oct 21, '18	Nov 18, '18	Dec 16, '18	Jan 13, '19	Feb 10, '19	Mar 10, '19
1		Obra : REHABILITACION PLANTA POTABILIZADORA FILTRACION RAPIDA 30 LPS Y ESTACION DE BOMBEO ACUEDUCTO PEDRO SANTANA-BANICA.	74.5 days	Mon 11/26/18	Fri 3/8/19		\$6,316,362.61	S	S	S	S	S	S
2		GASTOS DIRECTOS	22 days	Mon 11/26/18	Tue 12/25/18		\$273,987.13						
3		OBRA DE TOMA	5 days	Mon 11/26/18	Fri 11/30/18		\$115,939.60						
4		ILUMINACION DE AREA EXTERIOR EN OBRA DE TOMA	2 days	Mon 12/3/18	Tue 12/4/18	3	\$5,594.00						
5		CONSTRUCCION DE GARITA PARA OPERADOR	14 days	Mon 11/26/18	Thu 12/13/18		\$104,254.49						
6		PRELIMINARES	5 days	Mon 11/26/18	Fri 11/30/18		\$1,687.85						
7		HORMIGÓN ARMADO 180KG/CM2	1 day	Mon 12/3/18	Mon 12/3/18	6	\$20,454.44						
8		MURO DE BLOCKS	1 day	Tue 12/4/18	Tue 12/4/18	7	\$17,165.22						
9		TERMINACIÓN DE SUPERFICIE	2 days	Wed 12/5/18	Thu 12/6/18	8	\$23,092.41						
10		REVESTIMIENTO EN PAREDES	1 day	Fri 12/7/18	Fri 12/7/18	9	\$4,742.81						
11		INSTALACION SANITARIA	2 days	Mon 12/10/18	Tue 12/11/18	10	\$15,113.76						
12		PINTURA	2 days	Mon 12/10/18	Tue 12/11/18	10	\$9,297.73						
13		PUERTAS Y VENTANAS	2 days	Wed 12/12/18	Thu 12/13/18	12	\$7,670.29						
14		INSTALACIONES ELÉCTRICAS	1 day	Wed 12/12/18	Wed 12/12/18	12	\$5,029.98						
15		SEPTICO CON GALERIA DE INFILTRACION O CAMPO DE RIEGO (1.9 X 1.10 X 1.77) M	8 days	Fri 12/14/18	Tue 12/25/18	5	\$27,501.36						
16		REPLANTEO	1 day	Fri 12/14/18	Fri 12/14/18		\$500.00						
17		MOVIMIENTO DE TIERRA	1 day	Mon 12/17/18	Mon 12/17/18	16	\$1,606.06						
18		HORMIGON ARMADO EN 210 KG/CM2:	2 days	Tue 12/18/18	Wed 12/19/18	17	\$7,977.63						



Project: diagrama rehabilitacion
Date: Tue 10/30/18

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

Handwritten signature




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Cost	Oct 21, '18		Nov 18, '18		Dec 16, '18		Jan 13, '19		Feb 10, '19		Mar 10, '19		
								S	S	S	S	S	S	S	S	S	S	S	S	
19		MURO DE BLOCK	1 day	Thu 12/20/18	Thu 12/20/18	18	\$8,971.41													
20		TERMINACION DE SUPERFICIE	2 days	Fri 12/21/18	Mon 12/24/18	19	\$3,859.92													
21		INSTALACIONES:	1 day	Tue 12/25/18	Tue 12/25/18	20	\$4,586.34													
22		CAJA DE INSPECCION (0.70 X 0.7 X 0.75) M (2 U)	6.5 days	Fri 12/14/18	Mon 12/24/18	15SS	\$20,697.68													
23		REPLANTEO	1 day	Fri 12/14/18	Fri 12/14/18		\$300.00													
24		MOVIMIENTO DE TIERRA	1 day	Mon 12/17/18	Mon 12/17/18	23	\$320.48													
25		HORMIGON ARMADO EN: FC=180 KG/CM2	1 day	Tue 12/18/18	Tue 12/18/18	24	\$2,075.08													
26		MURO DE BLOCK	0.5 days	Wed 12/19/18	Wed 12/19/18	25	\$2,146.95													
27		TERMINACION DE SUPERFICIE	1 day	Wed 12/19/18	Thu 12/20/18	26	\$1,435.89													
28		INSTALACIONES DE:	1 day	Thu 12/20/18	Fri 12/21/18	27	\$4,468.34													
29		GALERIA DE INFILTRACION DE 9 M DE LONGITUD EN TUBERIA DE Ø4"	1 day	Fri 12/21/18	Mon 12/24/18	28	\$9,950.94													
30		ESTACION DE BOMBEO	23 days	Mon 12/24/18	Thu 1/24/19	29	\$483,270.62													
31		CASETA P/GENERADOR 100-200 KW	23 days	Mon 12/24/18	Thu 1/24/19		\$483,270.62													
32		REPLANTEO	1 day	Mon 12/24/18	Tue 12/25/18		\$500.00													
33		MOV. DE TIERRA	5 days	Tue 12/25/18	Tue 1/1/19	32	\$23,893.16													
34		HORMIGON ARMADO EN:	2 days	Tue 1/1/19	Thu 1/3/19	33	\$127,827.97													
35		MURO DE BLOQUES:	2 days	Thu 1/3/19	Mon 1/7/19	34	\$60,190.17													
36		TERMINACION DE SUPERFICIE	6 days	Mon 1/7/19	Tue 1/15/19	35	\$95,342.50													
37		PORTAJE	1 day	Tue 1/15/19	Wed 1/16/19	36	\$44,469.19													
38		INSTALACIONES ELECTRICAS	2 days	Tue 1/15/19	Thu 1/17/19	36	\$9,491.12													
39		REUBICACION DE GENERADOR ELECTRICO DE 100 KW (DISTANCIA APROXIMADA 20 MTS)	5 days	Thu 1/17/19	Thu 1/24/19	38	\$108,321.00													

Project: diagrama rehabilitacion
Date: Tue 10/30/18

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Cost	Oct 21, '18		Nov 18, '18		Dec 16, '18		Jan 13, '19		Feb 10, '19		Mar 10, '19	
								S	S	S	S	S	S	S	S	S	S	S	S
40		MOVIMIENTO DE TIERRA PARA ALIMENTADORES ELECTRICOS	3 days	Mon 12/24/18	Thu 12/27/18		\$13,235.51												
41		MURO DE GAVIONES PARA PROTECCION DE ESTACION DE BOMBEO	5 days	Fri 12/21/18	Fri 12/28/18	29SS	\$587,015.20												
42		MURO DE GAVIONES	5 days	Fri 12/21/18	Fri 12/28/18		\$587,015.20												
43		REHABILITACION DE PLANTA DE TRATAMIENTO DE 30 LPS	50 days	Fri 12/28/18	Fri 3/8/19	41	\$4,972,089.66												
44		INSTALACION DE TINACO PARA LA DISOLUCION DE SULFATO (CASA DE QUIMICO)	5 days	Fri 12/28/18	Fri 1/4/19		\$1,061,938.45												
45		SEDIMENTADOR, PRE-SEDIMENTADOR, FILTRO Y PRE-FILTRO	5 days	Fri 1/4/19	Fri 1/11/19	44	\$341,445.37												
46		ELIMINACION DE TUBERIA DE Ø6" PVC DESDE CAMARA DE ENTRADA HASTA EL CAMBIO DE PENDIENTE (INCLUYE MOVIMIENTO DE TIERRA)	1.5 days	Fri 1/11/19	Mon 1/14/19	45	\$23,830.49												
47		REPLANTEO	0.5 days	Fri 1/11/19	Fri 1/11/19		\$108.90												
48		MOVIMIENTO DE TIERRA	1 day	Mon 1/14/19	Mon 1/14/19	47	\$10,906.92												
49		TUBERIA DE REBOSE EN FILTRO EN ACERO DE Ø6" SCH-40	0.5 days	Fri 1/11/19	Fri 1/11/19	47SS	\$12,814.67												
50		TUBERIA DE DESAGUE CONECTADA A LA LINEA DE DESAGUE DEL DEPOSITO DE AGUA FILTRADA DE Ø8" ACERO SCH-40	1 day	Mon 1/14/19	Mon 1/14/19	49	\$47,453.51												

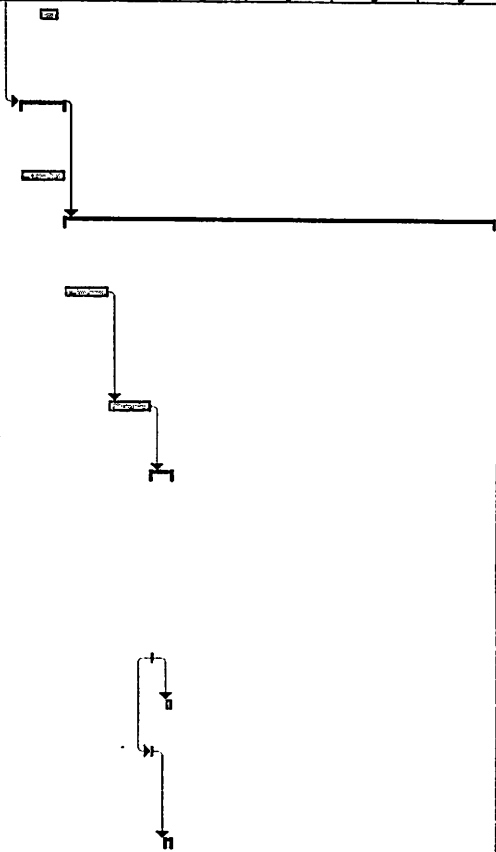

Project: diagrama rehabilitacion
Date: Tue 10/30/18

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Handwritten signature


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Cost	Oct 21, '18		Nov 18, '18		Dec 16, '18		Jan 13, '19		Feb 10, '19		Mar 10, '19	
								S	S	S	S	S	S	S	S	S	S		
51		REPLANTEO	0.5 days	Mon 1/14/19	Mon 1/14/19		\$36.30												
52		MOVIMIENTO DE TIERRA	0.5 days	Mon 1/14/19	Mon 1/14/19	51	\$3,355.71												
53		SUMINISTRO DE TUBERIA DE ACERO DE 8" C/PROTECCION ANTICORROSIVA	0.5 days	Mon 1/14/19	Mon 1/14/19	51SS	\$37,721.30												
54		COLOCACION DE TUBERIA DE ACERO DE 8" C/PROTECCION ANTICORROSIVA	0.5 days	Mon 1/14/19	Mon 1/14/19	53	\$2,239.70												
55		SUMINISTRO Y COLOCACION DE PIEZAS ESPECIALES	0.5 days	Mon 1/14/19	Mon 1/14/19	54SS	\$4,100.50												
56		REGISTRO EN MURO DE BLOCK DE 6 (1.30 X 1.30) M	3.5 days	Tue 1/15/19	Fri 1/18/19		\$39,396.60												
57		REPLANTEO	0.5 days	Tue 1/15/19	Tue 1/15/19	55	\$300.00												
58		HORMIGON ARNADO EN: FC=180 KG/CM2	0.5 days	Tue 1/15/19	Tue 1/15/19	57	\$2,432.91												
59		MURO DE BLOCK	0.5 days	Wed 1/16/19	Wed 1/16/19	58	\$2,976.64												
60		TERMINACION DE SUPERFICIE	1 day	Wed 1/16/19	Thu 1/17/19	59	\$3,230.43												
61		SUSTITUCION DE TUBERIA DE Ø8" PVC EN SALIDA DE AGUA DECANTADA (INCLUYE CORTE Y EXTRACCION TUBERIA PERFORADA EXISTENTE, PERFORACION Y COLOCACION DE TUBERIA PVC PERFORADA DE ACUERDO A DISEÑO Y COLUCCION)	1 day	Thu 1/17/19	Fri 1/18/19	60	\$30,456.62												

Project: diagrama rehabilitacion
Date: Tue 10/30/18

Task		Project Summary		Manual Task		Start-only		Deadline
Split		Inactive Task		Duration-only		Finish-only		Progress
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress
Summary		Inactive Summary		Manual Summary		External Milestone		




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Cost	Oct 21, '18		Nov 18, '18		Dec 16, '18		Jan 13, '19		Feb 10, '19		Mar 10, '19	
								S	S	S	S	S	S	S	S	S	S		
62		EXTRACCION, SUMINISTRO E INSTALACION DE VALVULAS EN BATERIA DE FILTROS	23 days	Tue 1/15/19	Thu 2/14/19	5655	\$759,561.44												
63		EXTRACCION DE VALVULAS	3 days	Tue 1/15/19	Thu 1/17/19		\$30,272.97												
64		SUMINISTRO E INSTALACION DE VALVULAS EN	5 days	Fri 1/18/19	Thu 1/24/19	63	\$309,895.95												
65		INTERCONEXION DE CAMARAS DE PRE-FILTRO	2 days	Fri 1/25/19	Mon 1/28/19	64	\$51,812.61												
66		FLOCULADOR	3 days	Tue 1/29/19	Thu 1/31/19	65	\$138,135.83												
67		SISTEMA DE LIMPIEZA	2 days	Fri 2/1/19	Mon 2/4/19	66	\$60,230.09												
68		EMBELLECIMIENTO CON GRAVILLA EXTRAIDA DEL PRE-FILTRO (SOLO REGADO Y LAVADO)	6 days	Tue 2/5/19	Tue 2/12/19	67	\$51,453.79												
69		LIMPIEZA INTERIOR DE TODAS LAS UNIDADES	5 days	Tue 2/5/19	Mon 2/11/19	67	\$49,727.21												
70		PINTURA GENERAL PLANTA DE TRATAMIENTO (INCLUYE RAPILLADO)	3 days	Tue 2/5/19	Thu 2/7/19	67	\$63,032.99												
71		LIMPIEZA FINAL Y CONTINUA	5 days	Fri 2/8/19	Thu 2/14/19	70	\$5,000.00												
72		CONSTRUCCION CASETA METALICA PARA SUSTANCIAS QUIMICAS (5.00 M X 5.00 M)	16 days	Fri 2/8/19	Fri 3/1/19	70	\$528,618.87												
73		PEDESTALES Y ESTRUCTURA METALICA	5 days	Fri 2/8/19	Thu 2/14/19		\$263,024.00												
74		INSTALACIONES ELECTROMECANICAS	5 days	Fri 2/15/19	Thu 2/21/19	73	\$196,073.22												

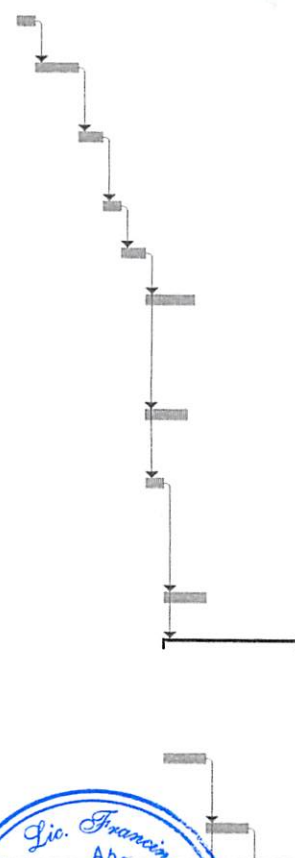

Project: diagrama rehabilitacion
Date: Tue 10/30/18

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			



Handwritten signature or initials.

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Cost	Oct 21, '18		Nov 18, '18		Dec 16, '18		Jan 13, '19		Feb 10, '19		Mar 10, '19	
								S	S	S	S	S	S	S	S	S	S		
75		ILUMINACION DE AREA EXTERIOR EN PLANTA	6 days	Fri 2/22/19	Fri 3/1/19	74	\$17,907.04												
76		CASETA DE GENERADOR EXISTENTE EN PLANTA	1 day	Fri 2/15/19	Fri 2/15/19	73	\$18,385.00												
77		VARIOS	1 day	Fri 2/8/19	Fri 2/8/19		\$33,229.61												
78		GASTOS INDIRECTOS	50 days	Fri 12/28/18	Fri 3/8/19		\$2,169,844.93												
79		GASTOS ADMINISTRATIVOS	50 days	Fri 12/28/18	Fri 3/8/19		\$165,860.71												
80		HONORARIOS PROFESIONALES	50 days	Fri 12/28/18	Fri 3/8/19		\$414,651.77												
81		SEGURO, POLIZAS Y FIANZAS	50 days	Fri 12/28/18	Fri 3/8/19		\$165,860.71												
82		SUPERVISION	50 days	Fri 12/28/18	Fri 3/8/19		\$207,325.88												
83		GASTOS DE TRANSPORTE	50 days	Fri 12/28/18	Fri 3/8/19		\$186,593.30												
84		LEY 6/86	50 days	Fri 12/28/18	Fri 3/8/19		\$41,465.18												
85		ITBIS DE LA 07-2007	50 days	Fri 12/28/18	Fri 3/8/19		\$74,637.32												
86		IMPREVISTOS	50 days	Fri 12/28/18	Fri 3/8/19		\$414,651.77												
87		MANTENIMIENTO Y OPERACION SISTEMA DE INAPA	50 days	Fri 12/28/18	Fri 3/8/19		\$414,651.77												
88		TRANSPORTE COMPLETIVO EQUIPO (IDA Y VUELTA)	50 days	Fri 12/28/18	Fri 3/8/19		\$80,000.00												
89		CODIA (SEGÚN MEMO No. 0972/2018 DJ)	50 days	Fri 12/28/18	Fri 3/8/19		\$4,146.52												

Project: diagrama rehabilitacion
Date: Tue 10/30/18

Task		Project Summary		Manual Task		Start-only		Deadline
Split		Inactive Task		Duration-only		Finish-only		Progress
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress
Summary		Inactive Summary		Manual Summary		External Milestone		

