



ID	Task Name	Duration	Start	Finish	Gantt Chart Timeline											
					01 Dec '13	18 Dec '13	11 Jan '14	04 Jan '14	28 Jan '14	24 Feb '14	17 Feb '14	11 Mar '14	04 Mar '14	28 Mar '14	22 Apr '14	15 Apr '14
1	<b>CPS-001-2014</b>	167 days	Mon 03/02/14	Fri 15/08/14	[Gantt bar spanning from 03/02/14 to 15/08/14]											
2	<b>RED DE DISTRIBUCION MARIA MONTÈS Y VALLE ENCANTADO</b>	100 days	Fri 07/02/14	Tue 03/06/14	[Gantt bar spanning from 07/02/14 to 03/06/14]											
3	PRELIMINARES	18 days	Tue 11/02/14	Mon 12/05/14	[Gantt bar spanning from 11/02/14 to 12/05/14]											
4	MOVIMIENTO DE TIERRA	93 days	Tue 11/02/14	Thu 29/05/14	[Gantt bar spanning from 11/02/14 to 29/05/14]											
5	EXCAVACION DE MATERIAL COMPACTO C/EQUIPO	86 days	Tue 11/02/14	Wed 21/05/14	[Gantt bar spanning from 11/02/14 to 21/05/14]											
6	ASIENTO DE ARENA	87 days	Thu 13/02/14	Sat 24/05/14	[Gantt bar spanning from 13/02/14 to 24/05/14]											
7	RELLENO COMPACTADO C/COMPACTADOR MECANICO	89 days	Sat 15/02/14	Thu 29/05/14	[Gantt bar spanning from 15/02/14 to 29/05/14]											
8	BOTE DE MATERIAL CON CAMION	20 days	Wed 19/02/14	Wed 28/05/14	[Gantt bar spanning from 19/02/14 to 28/05/14]											
9	SUMINISTRO Y COLOCACION DE TUBERIA	82 days	Fri 14/02/14	Tue 20/05/14	[Gantt bar spanning from 14/02/14 to 20/05/14]											
10	SUMINISTRO Y COLOCACION PIEZAS ESPECIALES	8 days	Wed 26/02/14	Tue 29/04/14	[Gantt bar spanning from 26/02/14 to 29/04/14]											
11	ANCLAJES	4 days	Fri 28/02/14	Tue 22/04/14	[Gantt bar spanning from 28/02/14 to 22/04/14]											
12	SUMINISTRO Y COLOCACION JUNTAS DRESSER	5 days	Wed 26/02/14	Mon 28/04/14	[Gantt bar spanning from 26/02/14 to 28/04/14]											
13	SUMINISTRO Y COLOCACION DE VALVULAS	8 days	Thu 27/03/14	Tue 29/04/14	[Gantt bar spanning from 27/03/14 to 29/04/14]											
14	CAJA TELESCOPICA	3 days	Wed 30/04/14	Sat 10/05/14	[Gantt bar spanning from 30/04/14 to 10/05/14]											
15	SUMINISTRO Y COLOCACION DE HIDRANTES	3 days	Mon 12/05/14	Tue 20/05/14	[Gantt bar spanning from 12/05/14 to 20/05/14]											
16	ACOMETIDA URBANA Ø1/2" (AGUA POTABLE) (500 U)	15 days	Mon 12/05/14	Wed 28/05/14	[Gantt bar spanning from 12/05/14 to 28/05/14]											
17	ASFALTO	8 days	Fri 07/02/14	Fri 30/05/14	[Gantt bar spanning from 07/02/14 to 30/05/14]											
18	CARPETA ASFALTICA	3 days	Sat 31/05/14	Tue 03/06/14	[Gantt bar spanning from 31/05/14 to 03/06/14]											
19	REDES DE DISTRIBUCION DE LOS AGRONOMOS, TRAMO MARIA MONTÈS Y VILLA DEL MAR	96 days	Fri 28/03/14	Thu 17/07/14	[Gantt bar spanning from 28/03/14 to 17/07/14]											
20	PRELIMINARES	15 days	Tue 01/04/14	Thu 05/05/14	[Gantt bar spanning from 01/04/14 to 05/05/14]											
21	MOVIMIENTO DE TIERRA	91 days	Tue 01/04/14	Tue 15/07/14	[Gantt bar spanning from 01/04/14 to 15/07/14]											
22	EXCAVACION DE MATERIAL COMPACTO C/EQUIPO	78 days	Tue 01/04/14	Mon 30/06/14	[Gantt bar spanning from 01/04/14 to 30/06/14]											



ID	Task Name	Duration	Start	Finish	01 Dec '13	24 18	11	19 Jan '14	04	28	09 Mar '14	24	17	11	04	28	15 Jun '14	04	28	22	15	08	03 Aug '14	
23	ASIENTO DE ARENA	80 days	Thu 03/04/14	Fri 04/07/14																				
24	RELLENO COMPACTADO C/COMPACTADOR MECANICO	83 days	Sat 05/04/14	Thu 10/07/14																				
25	BOTE DE MATERIAL CON CAMION	18 days	Wed 09/04/14	Tue 15/07/14																				
26	SUMINISTRO Y COLOCACION DE TUBERIA	76 days	Fri 04/04/14	Tue 01/07/14																				
27	SUMINISTRO Y COLOCACION PIEZAS ESPECIALES	7 days	Sat 12/04/14	Wed 04/06/14																				
28	ANCLAJES	3 days	Tue 15/04/14	Mon 19/05/14																				
29	SUMINISTRO Y COLOCACION JUNTAS DRESSER	4 days	Sat 12/04/14	Sat 24/05/14																				
30	SUMINISTRO Y COLOCACION DE VALVULAS	6 days	Mon 26/05/14	Thu 19/06/14																				
31	CAJA TELESCOPICA	2 days	Fri 20/06/14	Thu 26/06/14																				
32	SUMINISTRO Y COLOCACION DE HIDRANTES	2 days	Fri 27/06/14	Tue 01/07/14																				
33	CRUCES CANAL EN ACERO Ø6"	5 days	Fri 20/06/14	Wed 25/06/14																				
34	ACOMETIDA URBANA Ø1/2" (AGUA POTABLE) (500 U)	15 days	Sat 21/06/14	Tue 08/07/14																				
35	ASFALTO	7 days	Fri 28/03/14	Mon 14/07/14																				
36	CARPETA ASFALTICA	3 days	Tue 15/07/14	Thu 17/07/14																				
37	REDES DE DISTRIBUCION DE TRAMO MARIA MONTÉS Y PERPETUO SOCORRO (LA MONTAÑITA)	83 days	Mon 12/05/14	Fri 15/08/14																				
38	PRELIMINARES	12 days	Thu 15/05/14	Wed 02/07/14																				
39	MOVIMIENTO DE TIERRA	74 days	Thu 15/05/14	Fri 08/08/14																				
40	EXCAVACION DE MATERIAL COMPACTO C/QUIPO	61 days	Thu 15/05/14	Thu 24/07/14																				
41	ASIENTO DE ARENA	64 days	Sat 17/05/14	Wed 30/07/14																				
42	RELLENO COMPACTADO C/COMPACTADOR MECANICO	66 days	Tue 20/05/14	Mon 04/08/14																				
43	BOTE DE MATERIAL CON CAMION	14 days	Fri 23/05/14	Fri 08/08/14																				
44	SUMINISTRO Y COLOCACION DE TUBERIA	62 days	Mon 19/05/14	Tue 29/07/14																				

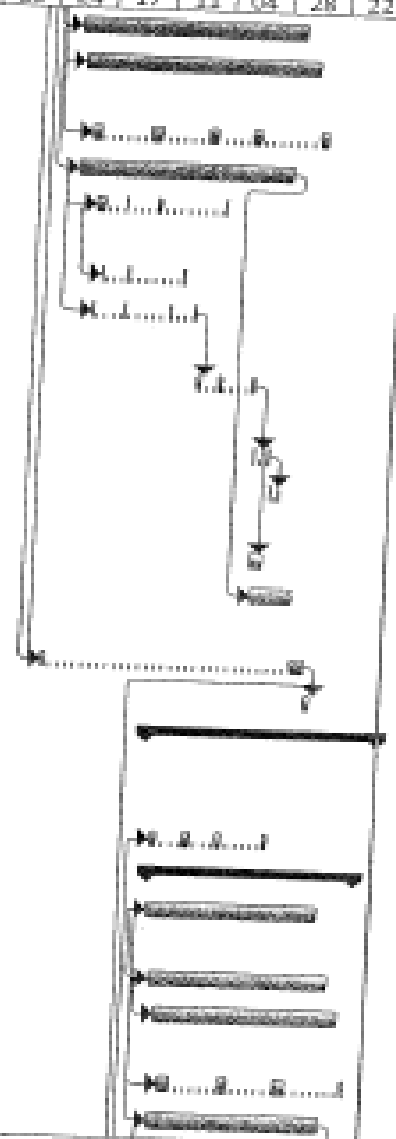

ID	Task Name	Duration	Start	Finish	01 Dec '13	19 Jan '14	09 Mar '14	27 Apr '14	15 Jun '14	03 Aug '14	21 Sep '14
45	SUMINISTRO Y COLOCACION PIEZAS ESPECIALES	6 days	Tue 27/05/14	Sat 21/06/14	24	18	11	04	28	24	17
46	ANCLAJES	2 days	Thu 29/05/14	Tue 10/06/14							
47	SUMINISTRO Y COLOCACION JUNTAS DRESSER	3 days	Tue 27/05/14	Fri 27/06/14							
48	SUMINISTRO Y COLOCACION DE VALVULAS	4 days	Sat 28/06/14	Wed 09/07/14							
49	CAJA TELESCOPICA	2 days	Thu 10/07/14	Wed 16/07/14							
50	SUMINISTRO Y COLOCACION DE HIDRANTES	2 days	Thu 17/07/14	Mon 21/07/14							
51	ACOMETIDA URBANA Ø1/2" (AGUA POTABLE) (700 U)	15 days	Sat 19/07/14	Tue 05/08/14							
52	ASFALTO	7 days	Mon 12/05/14	Tue 12/08/14							
53	CARPETA ASFALTICA	3 days	Wed 13/08/14	Fri 15/08/14							
54	VARIOS	4 days	Mon 03/02/14	Thu 06/02/14							
55	GASTOS INDIRECTOS	167 days	Mon 03/02/14	Fri 15/08/14							

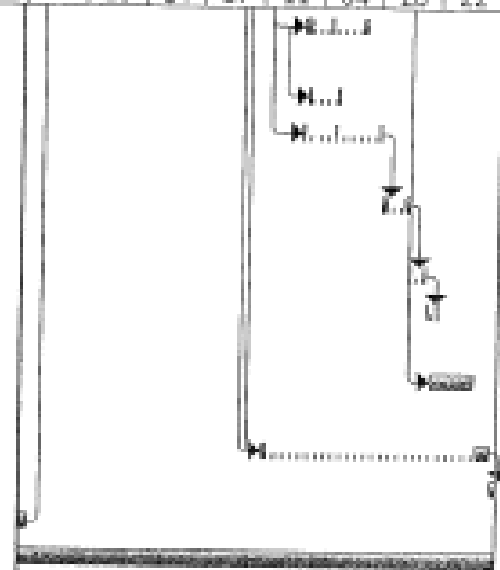

*R.G.*
